



Iglu Mascot 2 Areas of Demolition & Exclusion Zones

Through June & July 2024




Iglu Mascot 2 – Areas of Demolition & Exclusion Zones

Week **1** (Monday 17 June – Friday 21 June)

All work will be carried out between 7am and 5pm

Date	Scope of works	Impact to 3-9 Church Ave (East)	Impact to Iglu (South)
Mon 17 June	<ul style="list-style-type: none"> Cut back 2m of roof southern 	None	Exclusion
Tue 18 June	<ul style="list-style-type: none"> Cut back 2m of roof southern 	None	Exclusion
Wed 19 June	<ul style="list-style-type: none"> Cut back 2m of roof eastern Hand demolition ½ of southern brick wall 	None	<ul style="list-style-type: none"> Exclusion Potential mobile crane in driveway – minimal impact to vehicle access
Thu 20 June	<ul style="list-style-type: none"> Cut back 2m of roof eastern Hand demolition ½ of southern brick wall 	Exclusion	<ul style="list-style-type: none"> Exclusion Potential mobile crane in driveway – minimal impact to vehicle access
Fri 21 June	<ul style="list-style-type: none"> Cut back roof eastern Hand demolition ½ of southern brick wall 	Exclusion	<ul style="list-style-type: none"> Exclusion Potential mobile crane in driveway – minimal impact to vehicle access
Sat 22 June			
Sun 23 June			

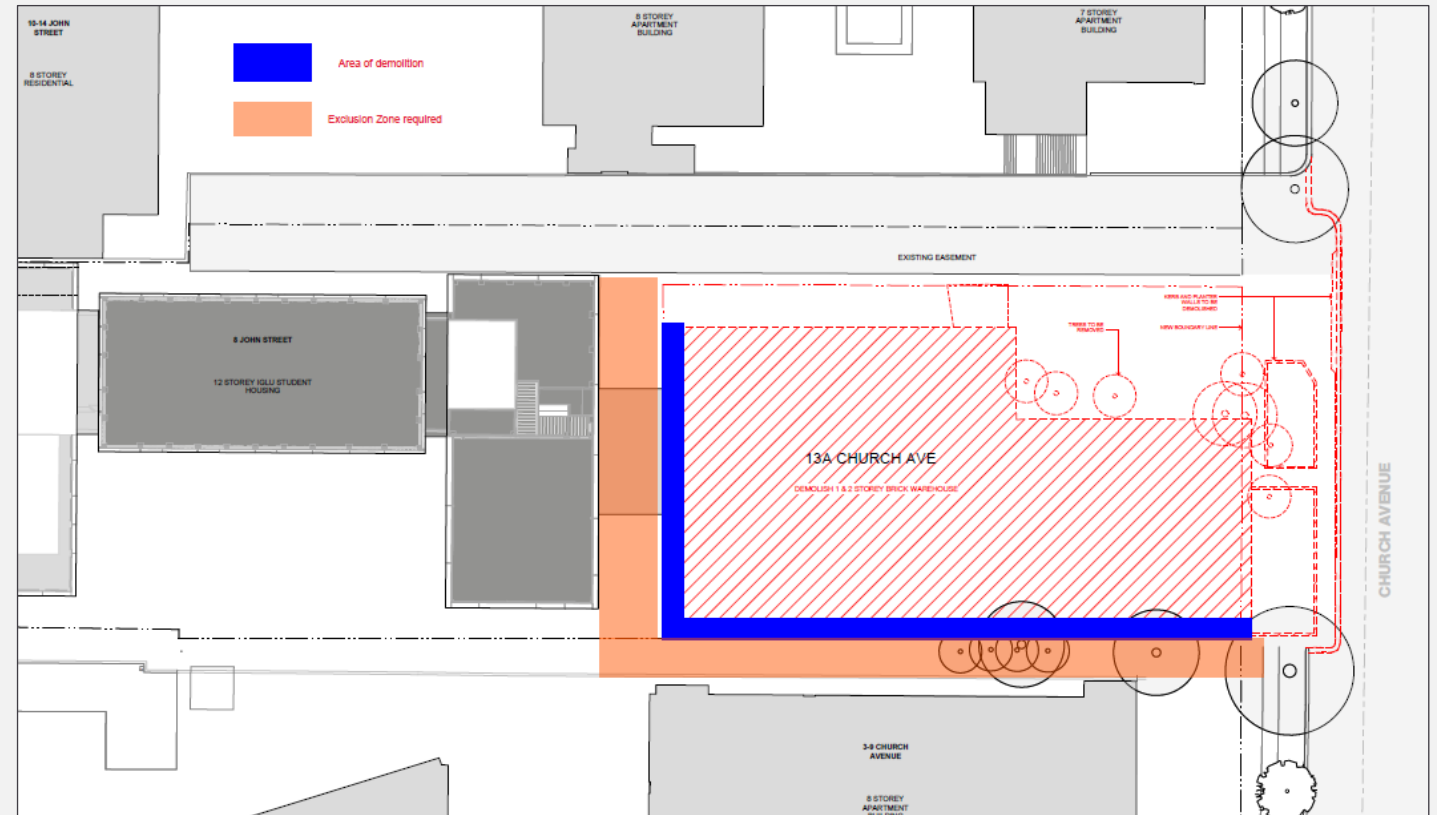


Iglu Mascot 2 – Areas of Demolition & Exclusion Zones

Week **2** (Monday 24 June – Friday 28 June)

All work will be carried out between 7am and 5pm

Date	Scope of works	Impact to 3-9 Church Ave (East)	Impact to Iglu (South)
Mon 24 June	<ul style="list-style-type: none"> Cut back 2m of roof eastern Hand demolition 1/3 of eastern wall 	Exclusion	None
Tue 25 June	<ul style="list-style-type: none"> Hand demolition 1/3 of eastern wall 	Exclusion	None
Wed 26 June	<ul style="list-style-type: none"> Hand demolition 1/3 of eastern wall Hand and machine demolition eastern and western walls 	Exclusion	None
Thu 27 June	<ul style="list-style-type: none"> Hand and machine demolition eastern and western walls 	Exclusion	None
Fri 28 June	<ul style="list-style-type: none"> Hand and machine demolition eastern and western walls 	Exclusion	None
Sat 22 June			
Sun 23 June			

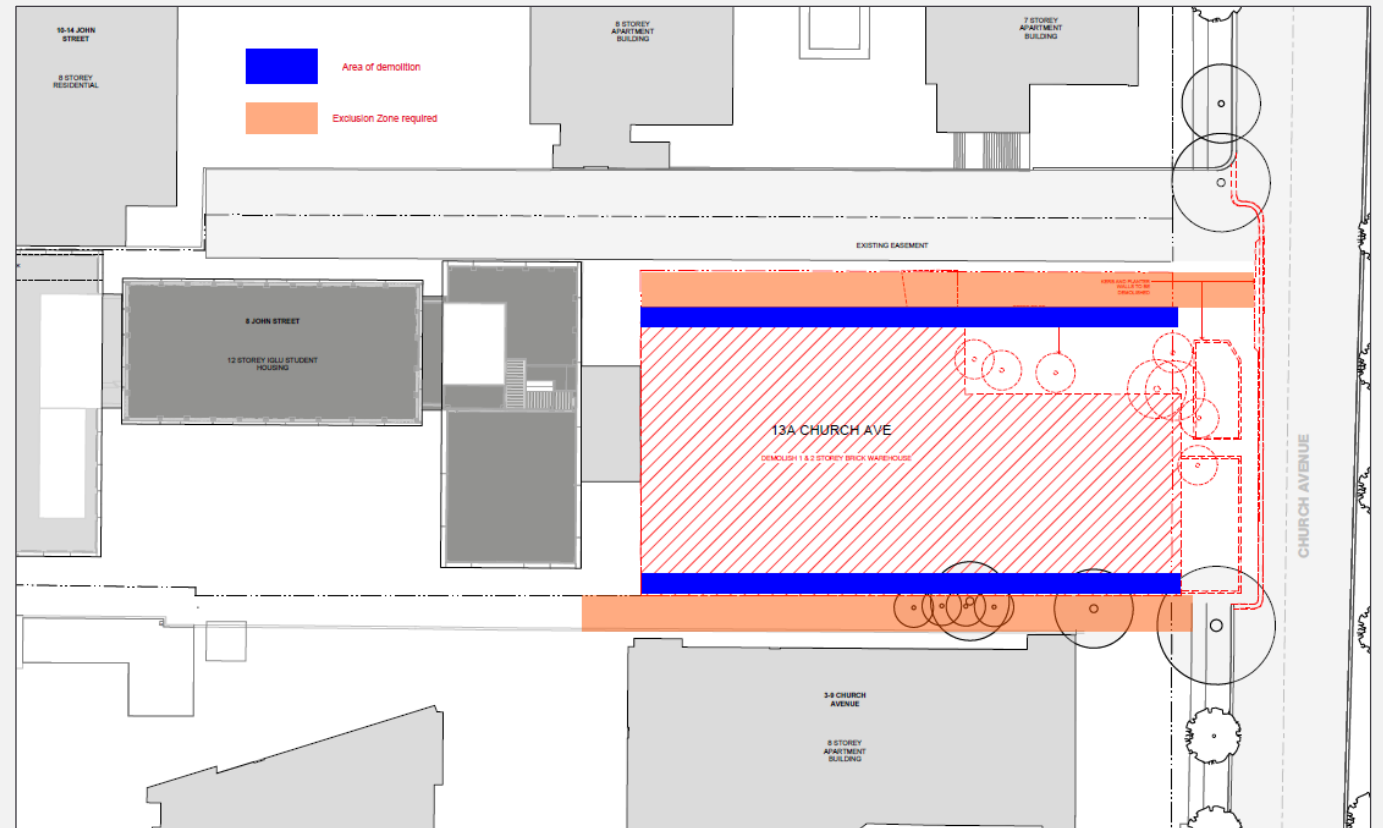


Iglu Mascot 2 – Areas of Demolition & Exclusion Zones

Week **3** (Monday 1 July – Friday 5 July)

All work will be carried out between 7am and 5pm

Date	Scope of works	Impact to 3-9 Church Ave (East)	Impact to Iglu (South)
Mon 1 July	<ul style="list-style-type: none"> Steel frame and roof removal Southern bays Suspended slab removal northern end 	Exclusion	Exclusion
Tue 2 July	<ul style="list-style-type: none"> Steel frame and roof removal Northern bays Suspended slab removal northern end 	Exclusion	Exclusion
Wed 3 July	<ul style="list-style-type: none"> Northern building demolition lower walls southern end near neighboring building 	Exclusion	None
Thu 4 July	<ul style="list-style-type: none"> Northern building demolition remaining lower walls 	None	None
Fri 5 July	<ul style="list-style-type: none"> Northern building demolition 	None	None
Sat 6 July			
Sun 7 July			

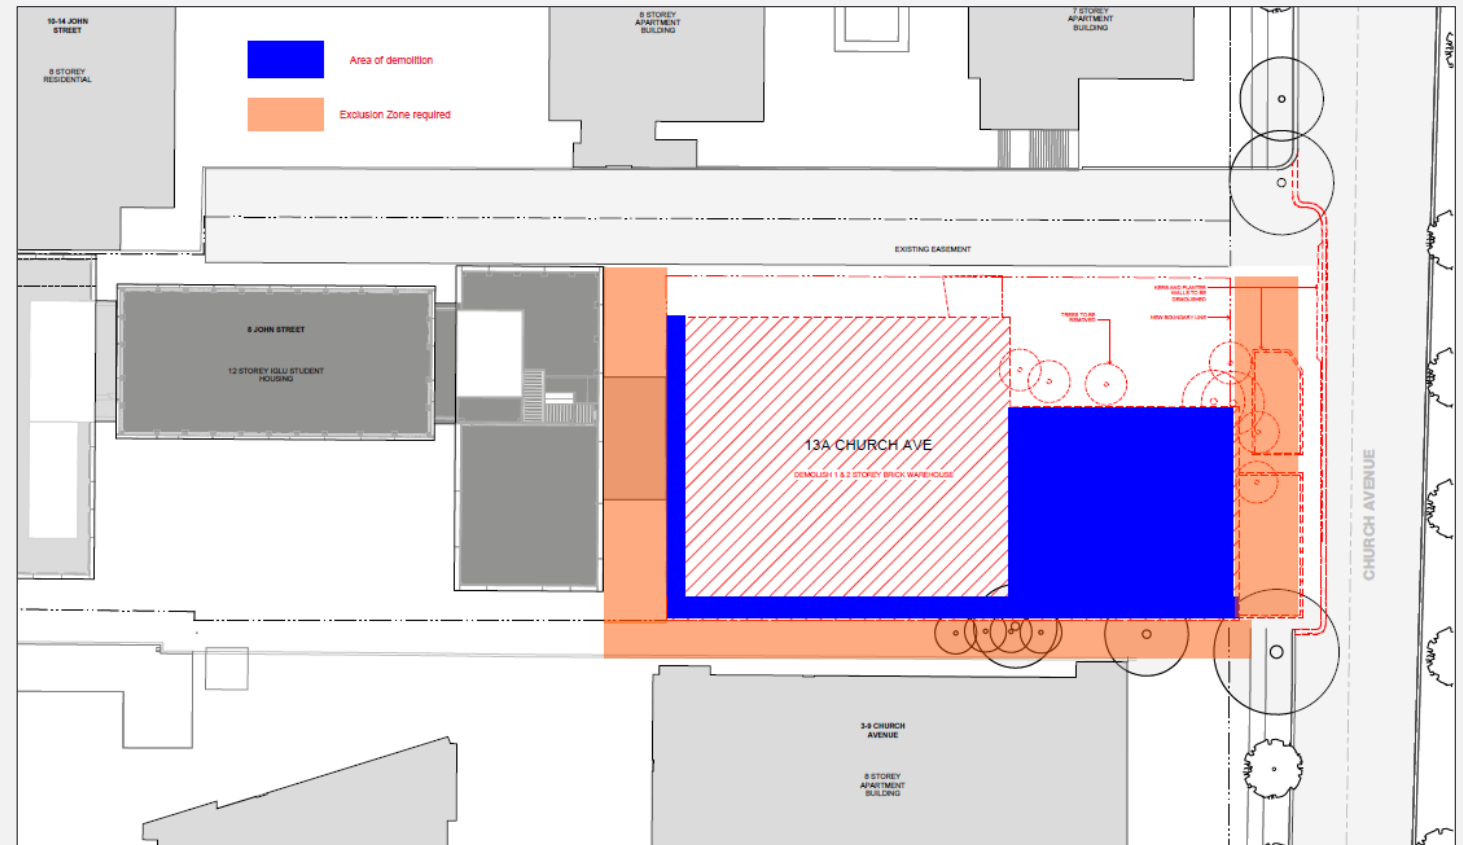

Iglu Mascot 2 – Areas of Demolition & Exclusion Zones

Week **4** (Monday 8 July – Friday 12 July)

All work will be carried out between 7am and 5pm

Date	Scope of works	Impact to 3-9 Church Ave (East)	Impact to Iglu (South)
Mon 8 July	<ul style="list-style-type: none"> Machine demolition Load out/clean up 	None	None
Tue 9 July	<ul style="list-style-type: none"> Machine demolition Load out/clean up 	None	None
Wed 10 July	<ul style="list-style-type: none"> Machine demolition Load out/clean up 	None	None
Thu 11 July	<ul style="list-style-type: none"> Machine demolition Load out/clean up 	None	None
Fri 12 July	<ul style="list-style-type: none"> Machine demolition Load out/clean up 	None	None
Sat 6 July			
Sun 7 July			

